

SCOPE MANAGEMENT PACKET

Most2baly Youth Summer Bootcamp | Version 1.0 | May 19, 2026

PM C1 Team 2 | Hesham Mohamed • Ali Elgazzar • Doha Ahmed • Ahmed Zaki

Introduction


This Scope Management Packet defines the complete work breakdown for the Most2baly Youth Summer Bootcamp. It applies the 100% Rule to ensure no work is missing or duplicated, establishes a Scope Creep Shield to defend the project against unauthorized changes, and introduces an Advanced Change Control technique to manage future requests professionally.

Step 1: Work Breakdown Structure (The Project DNA)

What is the WBS?

The Work Breakdown Structure (WBS) is the complete decomposition of all project work into manageable components. Using the **100% Rule**, every piece of work — and only that work — is captured. Nothing is missing; nothing is duplicated.

WBS Hierarchy Diagram

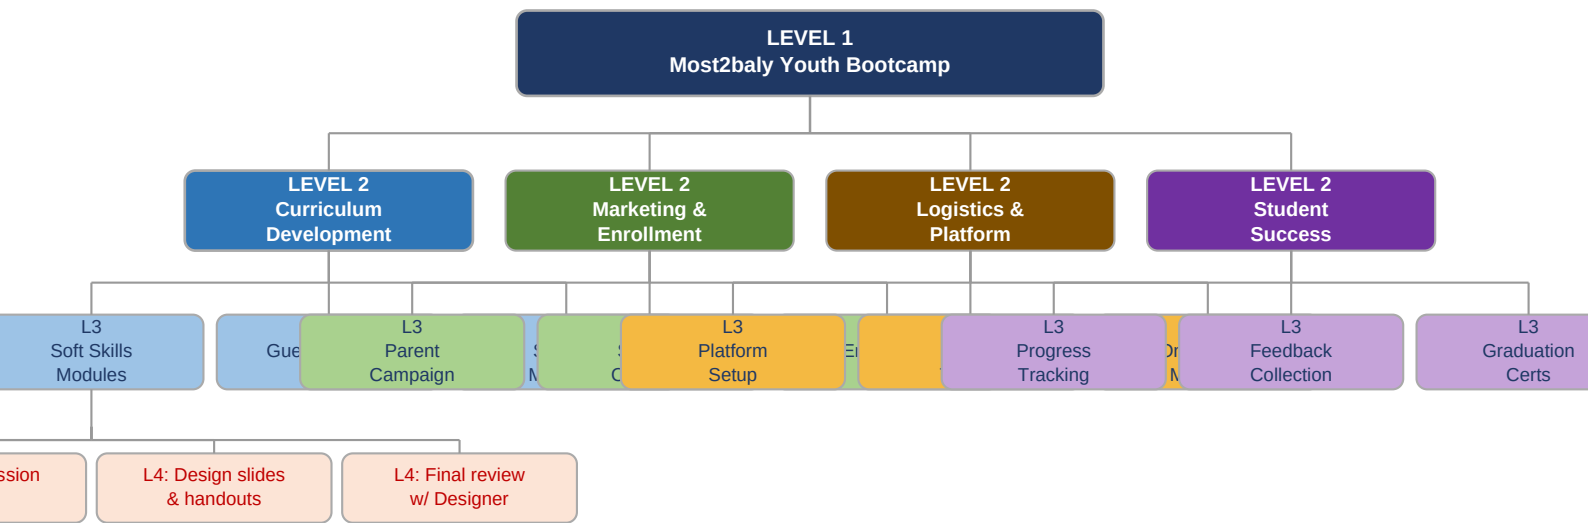

* Level 4 tasks shown for 'Soft Skills Modules' work package only (100% Rule applied)

Figure 1: 4-Level WBS for Most2baly Youth Bootcamp — 100% Rule Applied

Level 2 Deliverables — Explained

Level 2 Deliverable	What It Contains	Why It's Critical
---------------------	------------------	-------------------

Curriculum Development	All 4-week bootcamp content: soft skills modules, guest speaker sessions, and session materials	Without content, there is no bootcamp. This is the core product.
Marketing & Enrollment	Parent-targeted campaigns, student outreach, and enrollment management to hit 50 students	Without 50 students, the pilot is financially unviable (Sponsor constraint).
Logistics & Platform	Online platform setup, technical testing, and student onboarding materials	A technical failure during a live session could destroy student trust instantly.
Student Success	Progress tracking, weekly feedback collection, and graduation certificates	80% graduation rate is a key success criterion — this track ensures it.

SCOPE MANAGEMENT PACKET

Most2baly Youth Summer Bootcamp | Version 1.0 | May 19, 2026

PM C1 Team 2 | Hesham Mohamed • Ali Elgazzar • Doha Ahmed • Ahmed Zaki

Step 2: The Scope Creep Shield

The Stakeholder Request

Stakeholder Request (SCOPE CREEP ALERT ■)

"Since we are doing a digital marketing session, can we also build a full Social Media Agency for the students to run?"

The Critical WBS Question

Before responding to any change request, the Project Manager must ask one question:

"Is this work currently captured anywhere in our approved WBS? If not, it is outside our defined scope."

The Shield Script — PM Response Using Phase 2 Backlog Technique

The following is the Project Manager's professional response to the stakeholder's request:

Shield Script ■■

"Thank you for this idea — building a Social Media Agency for our students is genuinely exciting and aligns with Most2baly's mission."

I am formally adding this to our Phase 2 Backlog, where it will be properly scoped, budgeted, and planned as a priority initiative for future development.

Phase 2 Backlog — Brilliant Ideas for Later

The following ideas are currently **OUT OF SCOPE** for the 3-month launch but are formally recorded in the Phase 2 Backlog for future development:

#	Idea	Why Out of Scope Now	Why It Belongs in Phase 2
1	Social Media Agency for Students	Requires separate budget, curriculum, and platform — far beyond \$5,000 cap	Strong brand extension; builds on the digital skills angle naturally
2	Alumni Network & Mentorship Program	Bootcamp hasn't launched yet — no alumni exist to build a network	High retention value; converts graduates into Most2baly brand ambassadors

SCOPE MANAGEMENT PACKET

Most2baly Youth Summer Bootcamp | Version 1.0 | May 19, 2026

PM C1 Team 2 | Hesham Mohamed • Ali Elgazzar • Doha Ahmed • Ahmed Zaki

Step 3: Advanced Technique — Change Request Tax + Budget Bank

Technique A: The Change Request Tax ■

Anyone who wants to propose a change to the project scope, budget, or timeline must complete this 3-question form. The 'tax' here is the effort required to think through and justify the change — which naturally filters out impulsive requests and protects the project from scope creep.

CHANGE REQUEST FORM — Most2baly Youth Bootcamp
Submitted by: _____ Date: _____
Question 1: What exactly is the change you are proposing? (Be specific — what will be added, removed, or modified?)
Answer: _____ _____
Question 2: Why is this change necessary? What problem does it solve or opportunity does it capture? (Explain the business justification clearly.)
Answer: _____ _____
Question 3: What is the estimated impact on Scope / Budget / Timeline? (Quantify where possible — e.g., '+\$500', '+2 weeks', 'adds 1 new module')
Scope Impact: _____
Budget Impact: _____
Timeline Impact: _____
Sponsor Approval Required? ☐ Yes (if impact > \$500 or > 3 business days)
PM Decision: ☐ Approved ☐ Rejected ☐ Deferred to Phase 2 Backlog
PM Signature: _____ Date: _____

Technique B: The Budget Bank ■

A smart PM never spends 100% of the budget. Setting aside a contingency reserve protects the project when unexpected costs arise — without going back to the Sponsor for more money.

Budget Bank Calculation

Emergency Use Case

Total Budget: \$5,000 Contingency Reserve: 15% = \$750 Operating Budget: \$4,250 The \$750 Budget Bank is held in reserve and only released by the PM for approved emergencies.	Scenario: Platform Technical Failure If the primary hosting platform crashes 2 days before Go-Live, the \$750 Budget Bank covers emergency migration to a backup platform (e.g., Zoom Webinar or Teachable) — keeping the July 24 launch date intact without Sponsor approval for extra funds.
---	--

■ Summary: Scope Management at a Glance
WBS (100% Rule) → Defines ALL work. Nothing missing. Nothing extra. Phase 2 Backlog → Smart way to say YES to ideas without derailing the project. Change Request Tax → Forces stakeholders to think before they ask. Budget Bank (\$750) → Emergency fund that keeps the project alive without Sponsor intervention.
