


SCHEDULING MASTER DOCUMENT

Most2baly Youth Summer Bootcamp | CriticalPath & Gantt Chart

PM C1 Team 2 | Hesham Mohamed • Ali Elgazzar • Doha Ahmed • Ahmed Zaki

Step 1: Network Diagram — Critical Path Method (CPM)

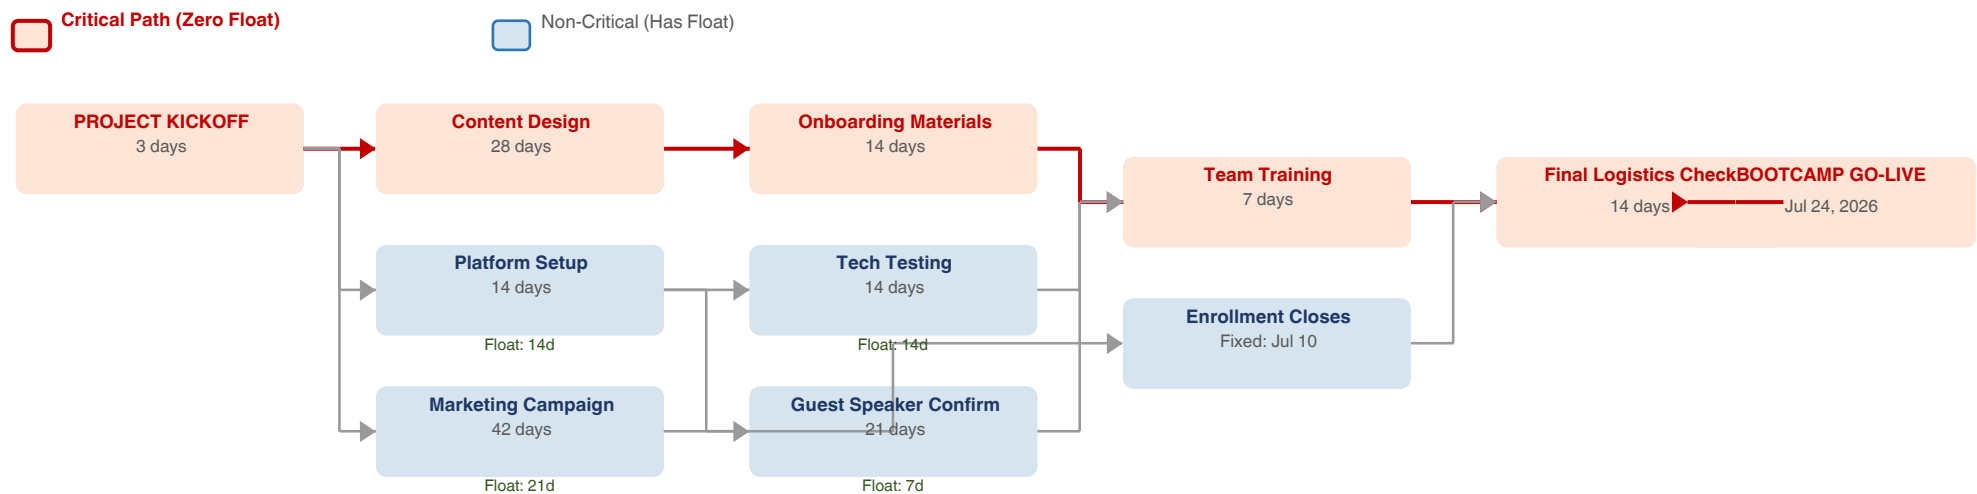


Critical Path: Kickoff → Content Design → Onboarding → Team Training → Final Check → GO-LIVE

SCHEDULING MASTER DOCUMENT

Most2baly Youth Summer Bootcamp | Critical Path & Gantt Chart | May 22, 2026

PM C1 Team 2 | Hesham Mohamed • Ali Elgazzar • Doha Ahmed • Ahmed Zaki

Step 2: Most2baly Youth — Gantt Chart

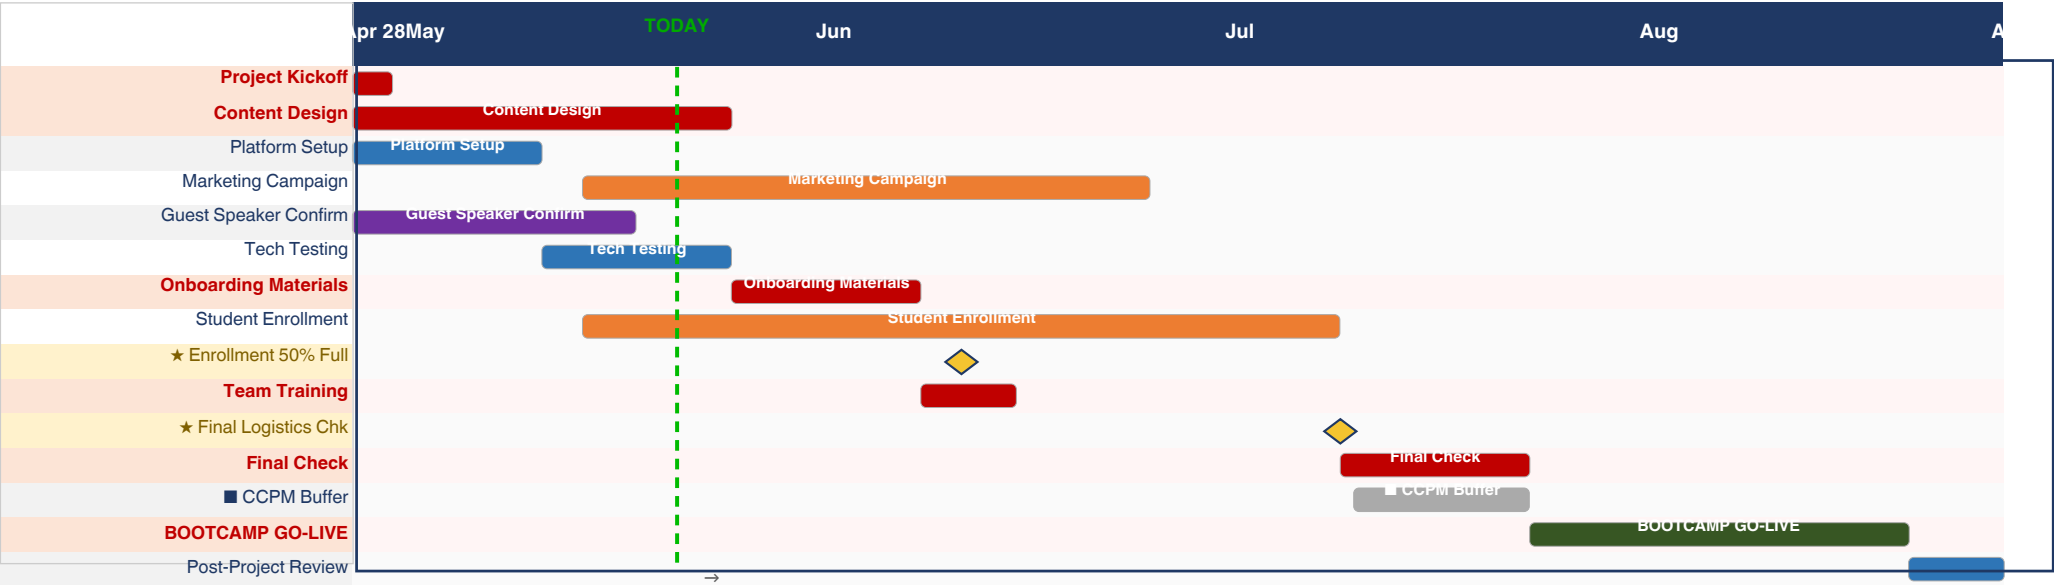

SCHEDULING MASTER DOCUMENT

Most2baly Youth Summer Bootcamp | Critical Path & Ganтт Chart

PM C1 Team 2 | Hesham Mohamed • Ali Elgazzar • Doha Ahmed • Ahmed Zaki

■ Step 3: CCPM Buffer — ■ ■ ■ ■ Parkinson's Law

Critical Chain Duration	63 days (Apr28 → Jul 10)
Project Buffer (20%)	13 days
Internal Team Deadline	July 11, 2026
Official Sponsor Deadline	buffer, July 24, 2026
Buffer Window	July 11 → July 24

■ Pro-Hack: Parkinson's Law Shield

"Team, our deadline is July 11 — that's the date on your boards. The 13 days after that are my emergency buffer, not polish time. The Spon

■ NZTA Lesson: Resource Leveling

:

Conflict			
Marketing Team Overload (May 15–26)	Assigned : - Marketing Campaign - Onboarding Materials = 200%utilization	Onboarding Materials Content Designer. Marketing Team focused Campaign = 80% utilization	Campaign 50-student target Onboarding Materials
PM Bottleneck (Jun 9–16)	PM : - TeamTraining - GuestSpeaker Coord. - WeeklySponsor Report	Guest Speaker Coordination Content Designer . PM Training + Report	Training Guest Speakers prepared

■ Scheduling Summary

Critical Path: Kickoff → Content Design → Onboarding Materials → Team Training → Final Check → GO-LIVE (63 days | Zero Float)

Non-Critical: Platform Setup (14d float) | Marketing Campaign (21d float) | Guest Speaker Confirm (7d float)

Milestones: ★ Enrollment 50% Full (Jun 12) | ★ Final Logistics Check (Jul 10)

CCPM Buffer: 13 days (Jul 11→24) — Team deadline = Jul 11 | Sponsor deadline = Jul 24

Resource Leveling: Marketing Team & PM conflicts resolved → max 80% utilization on all critical tasks
